

# Accessible Improvement Program (AIP) update

BART Accessibility Task Force (BATF) November 21, 2024

FTA-CA-2017-029-00 FTA-CA-2018-084-00





#### **Current Stations Under Construction**



- Castro Valley
- Lafayette
- Rockridge
- Richmond
- North Berkeley
- MacArthur

- Fruitvale
- San Leandro
- Bay Fair
- Hayward
- Fremont


# **Project Overview**



Key Information As of November 12, 2024	
Monetary % complete:(Billed to date)	84%
Notice to Proceed	July 10, 2023
Contract Duration	500 Calendar days
Contract Time Elapsed	484 Calendar Days (97%)
Remaining Contract Time	16 + 62 Calendar Days
Contract Completion	November 20, 2024
The contractor projected the completion date on the June schedule update. (subject to review of TIA001)	January 30, 2025
Crew size	Approx. 10 Field Workers
Outstanding NCRs	0

# **Best Management Practices (BMPs)**



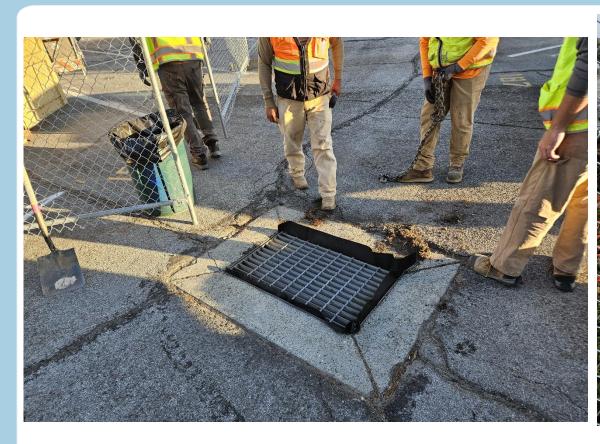



#### **General Scope of Work at ALL Stations**



#### **Scope of Work:**

- Replacement of curb ramps, sidewalks, accessible paths, loading zones at bus and passenger
- Installed new wall protrusion detection
- Replacement of courtesy phones
- Replacement of handrails
- Installation of elevator lobby light
- Remove and install new stainless Steel composite panels inside the stations

#### **Fremont Station - West**








# **Bay Fair**



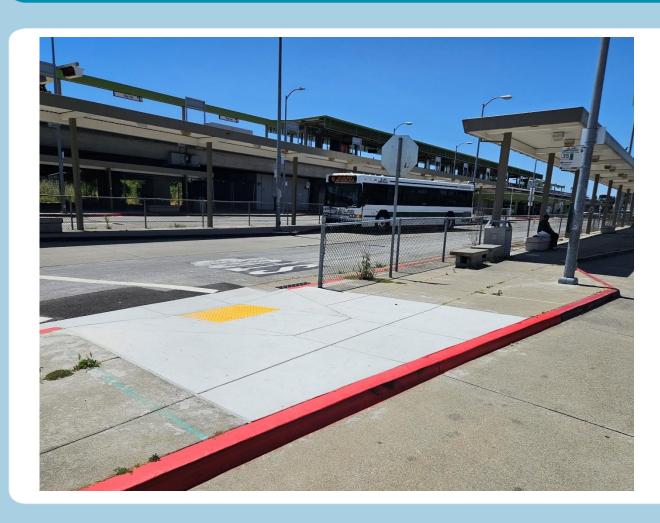




## **Hayward (continued)**





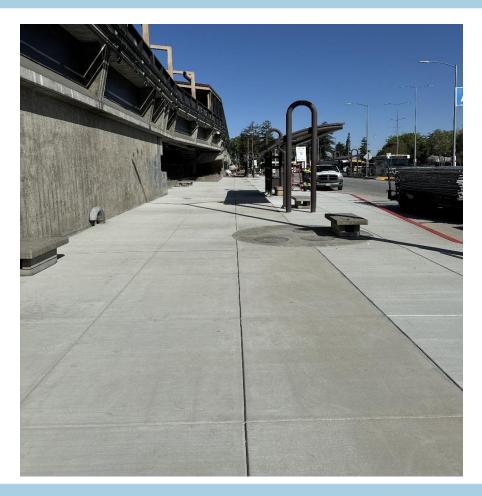

## **Castro Valley**









#### **Fruitvale**



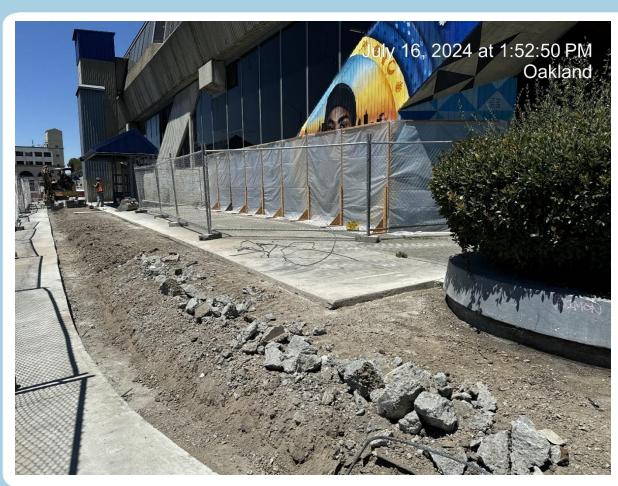


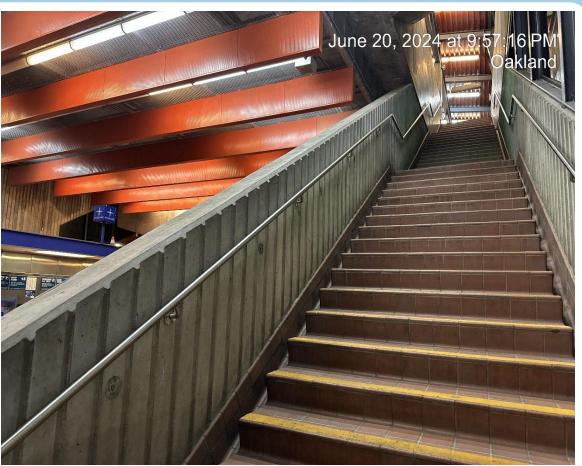

#### **San Leandro**





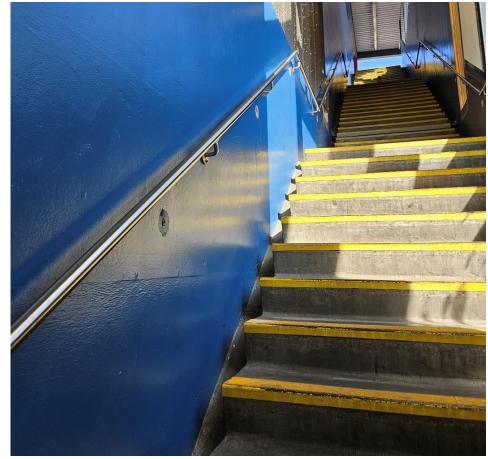

#### **MacArthur**









# Lafayette




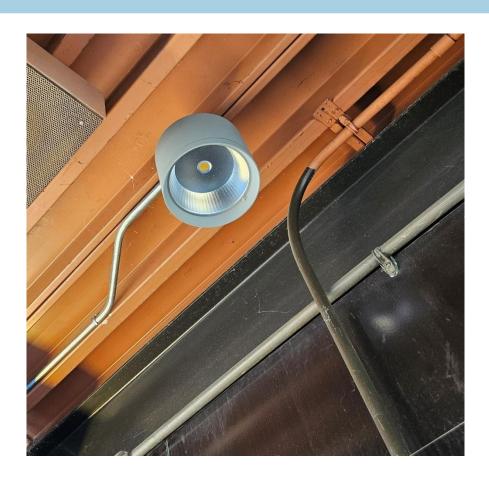


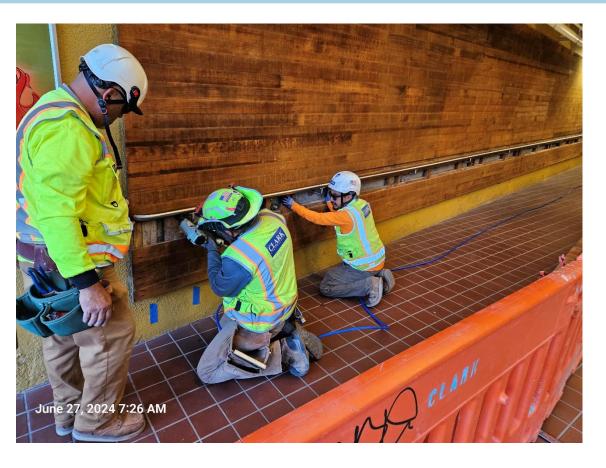

# **North Berkeley**



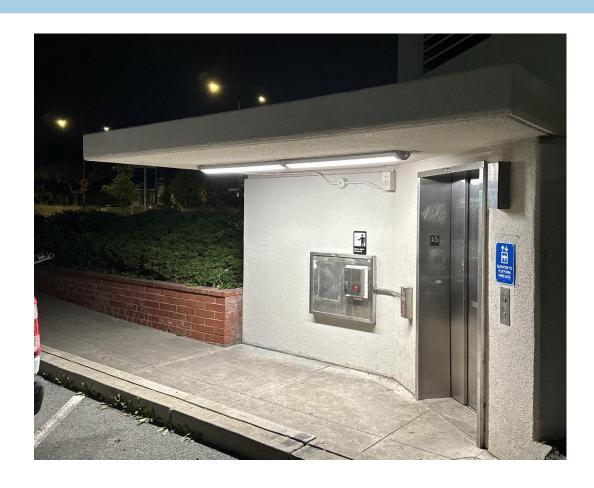

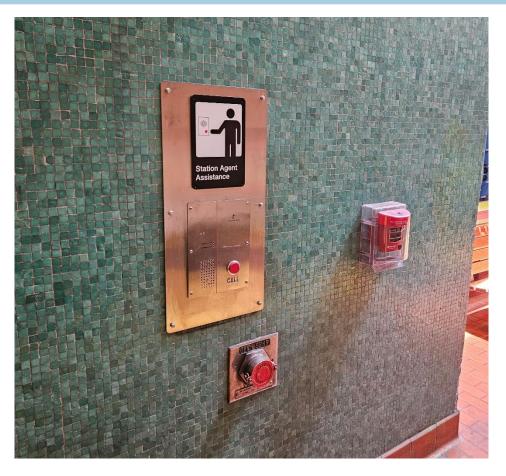

#### Richmond









# Thank you. Questions?
