



▶ Accessibility Improvement Program (AIP) Update

July 24, 2025 | BATF (BART Accessibility Task Force)



FTA-CA-2017-029-00
FTA-CA-2018-084-00



Work Completed

Stations

- Castro Valley
- Lafayette
- Rockridge
- Richmond
- North Berkeley
- MacArthur
- Fruitvale
- San Leandro
- Bay Fair
- Hayward
- Fremont



Project Overview

Contract No. 15NU-145 As of June 18, 2025	
Monetary % complete (Billed to date):	96.75%
Notice to Proceed	July 10, 2023
Contract Duration	500 Calendar days
Contract Completion	November 20, 2024
Contract Punchlist Completion	March 15, 2025
Crew size	Approx. 10 Field Workers
Outstanding NCRs	0
Final Construction Cost	9,660,388.00

General Scope of Work

Scope of Work:

- Replacement of curb ramps, sidewalks, accessible paths, bus and passenger loading zone
- Installation of new wall protrusion detections
- Replacement of courtesy phones
- Replacement of handrails
- Installation of elevator lobby lighting
- Removal and installation of new stainless steel composite panels inside stations

Fremont Station - West



Bay Fair

Accessible ramp reconstructed to correct slopes



**Replace courtesy phones with
ADA compliant call box**



Hayward

Accessible ramp reconstructed to correct slopes



Sidewalk reconstructed to correct slope



Castro Valley

Sidewalk reconstructed to correct slope



Accessible ramp reconstructed to correct slopes



Fruitvale



San Leandro



MacArthur



Replace courtesy phones with ADA compliant call boxes

Lafayette




North Berkeley

Replace elevator lobby lighting



Replace courtesy phone with ADA compliant call box

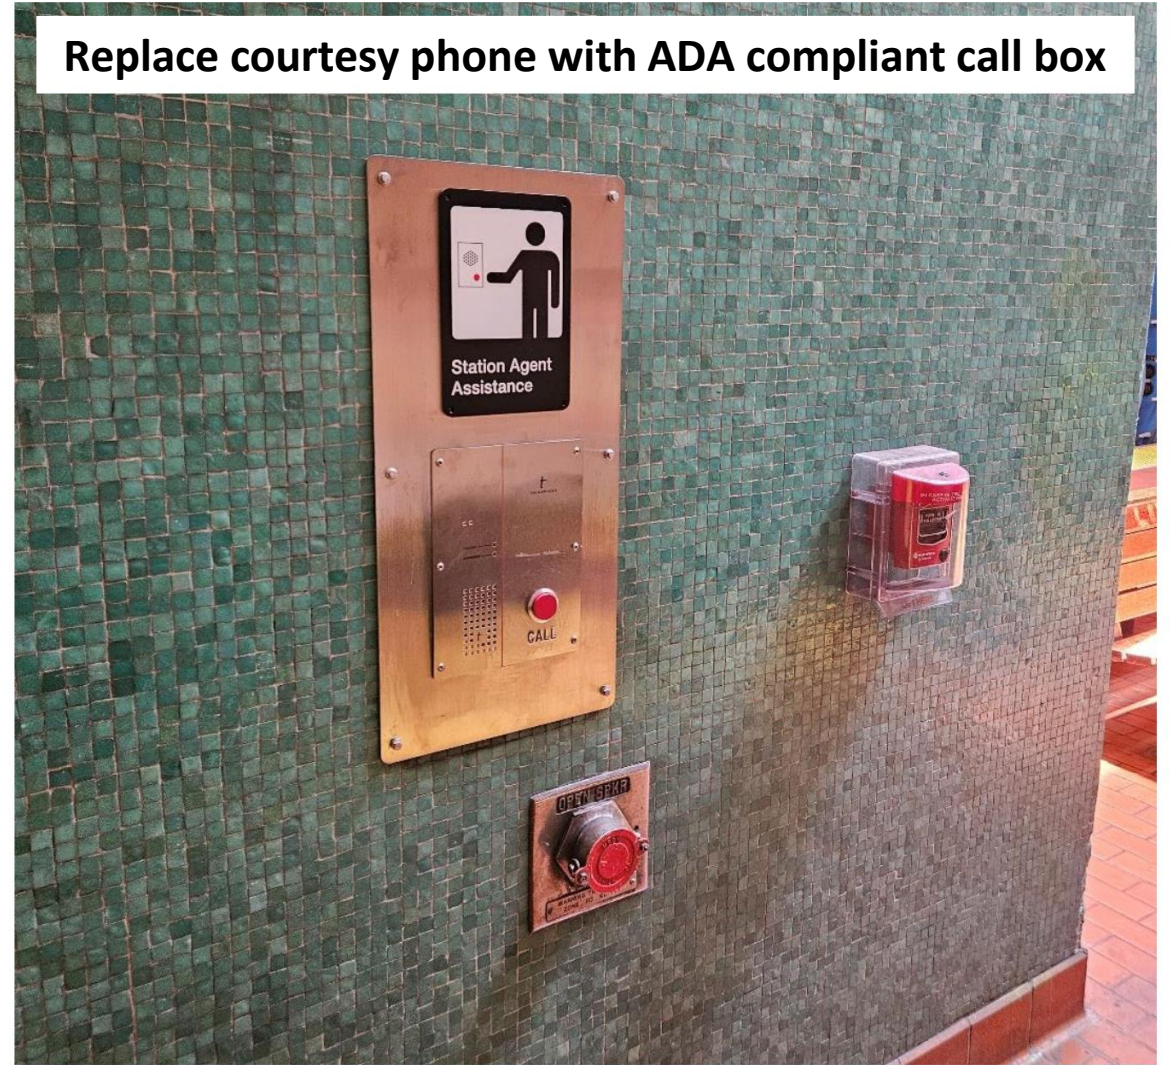

Richmond

Replace courtesy phones with ADA compliant call boxes



Thank You

